

Steve E.

TBD

TBD

N/A

Pending

Leon C

Steve E.

TBD

TBD

# **SDCCD MIRAMAR COLLEGE - CAPITAL RENOVATION RENEWALS**

Measure HH Fire Suppression (Bldg. W)		Projects (Bldg.)	Status	Duration	Estimate	Status
Architect:	РВК	7	Phase	Est. Date	Construct Cost	Description
Engineer (Fire): Region 3 Project Manager: Construction Manager:	Leaf Engineering Leon Cavallo. Steve Evanco	Fire Suppression	Award	7/17/25	\$390,408	Pre-award review conducted. Award rending the 7/17/25 Board meeting
Inspector: Contractor:	Phil San Filippo TBD	Roofs Replacement	Planning	7/14/25	TBD	Multiple bldgs.: (CDC, Police, Science, Bus Humanities, work package work defined, a proposal submission.
Roof Renovations (Multiple Bldgs.)		HVAC Replacement	Planning	7/14/25	TBD	Multiple bldgs.: work package work defin proposal submission.
Architect: Engineer: Region 3 PM:	Pending N/A Leon C.	IDF/MDF Rooms (HVAC Assessment)	Planning	7/7/25	TBD	This consultant is working with the IT depa the programming needs for these specific rooms.

## Project Insight (Look Ahead)

## Fire Suppression (Bldg. W):

6/24/25: Post Bid interview

7/17/25: Recommend contract for Board Award

## **Roof Renovation Multiple Bldgs.)**:

HVAC Renovation (Multiple Bldgs.) :

7/7/25: Roof work packages developed 7/14/25: Scope sent to architect for design proposal 7/21/25: Contract established, design started

#### IDF / MDF Rooms (HVAC Assessment)


**HVAC Renovation (Multiple Bldgs.)** 

N/A	
Pending	
Leon C	
Steve E.	
TBD	
TBD	

## IDF/MDF Rooms (HVAC Assessment):

7/7/25: Scope review being conducted for IT programming and design proposal

7/14/25: Scope being sent to Engineer for a design proposal

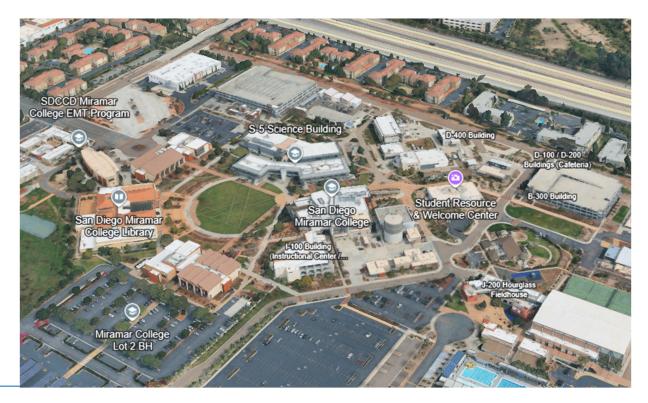

PROJECT FEATURES: These Region 3 Capital Renovation Renewal projects represent work in multiple buildings on each campus and will improve the college environment. Each project on the list will be assessed by our architectural and construction management teams, once scope assessments happens, then the scope can be defined and project packages assembled, and put out to bid for construction.

Inspector:

Contractor:

Architect:

Engineer (Mech):

Construction Manager:

Region 3 PM:

Inspector:

Contractor:

Construction Manager:

# CUMMING GROUP

## **Upcoming Projects**

The following projects are scheduled to happen with the next 3 weeks:

- Electrical site scope work package assessments for design contract

- Pool deck re-surfacing replacement

- Gym exterior painting and bird screen gutter replacement

- Data Center refreshed, looking at HVCA and IT scopes

## **Project Site Plan**

The projects are within the boundaries of Hillery Drive to Gold Coast Drive (north to south) and Black Mountain Road to North & South Campus Drive (east to west)

# Buildings and Programs (w/scope identified)

K, N, A, S-5 (Science), P, H (Arts & Humanities), L, F-1 (Aviation), F-2 (CDC), M (Business & Math), N (Administration), C-1, W (Distribution & Computing Center), I, R, J-1 (Gym), J (See the campus map for the full building designations)

**PROJECT PROFILE — SDCCD Miramar College Multiple Projects** 

## award review conducted. Award recommendation

ole bldgs.: (CDC, Police, Science, Business & Math, and nities, work package work defined, awaiting design

ple bldgs.: work package work defined, awaiting design

consultant is working with the IT department to outline rogramming needs for these specific MDF and IDF
